ॐ

First and Final Bill

190014

DOR => 03/05/2018

M.A.R. 57 (Rule 116)

Measurement Book

No. C/09

Serial No.....

Name of work.....From.....To.....

Name of Contractor of nature of Agency.....M/S KRIDL.....

Date of commencement of work.....

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
	Name of the work: Improvement works at Dog kennal at Sy no: 51 Mallasandra ward no: 13 of project subdivision Dasarahalli zone.						
	Estimate at Rs 39.00 Lakhs.						
	Job code No: 013-17-000037						
	AS NO: → JC/DZ/PR/AS/84/2017-18 dated 14/3/2017						
	TS NO: → CE/TS/50/2017-18 dated 24/5/2017						
	W.O.NO: → BBMP/EE/PD/W.O/000014/2017-18 dated 01-01-2018						

Scanned by CamScanner

MEASUREMENT BOOK

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
							W N E

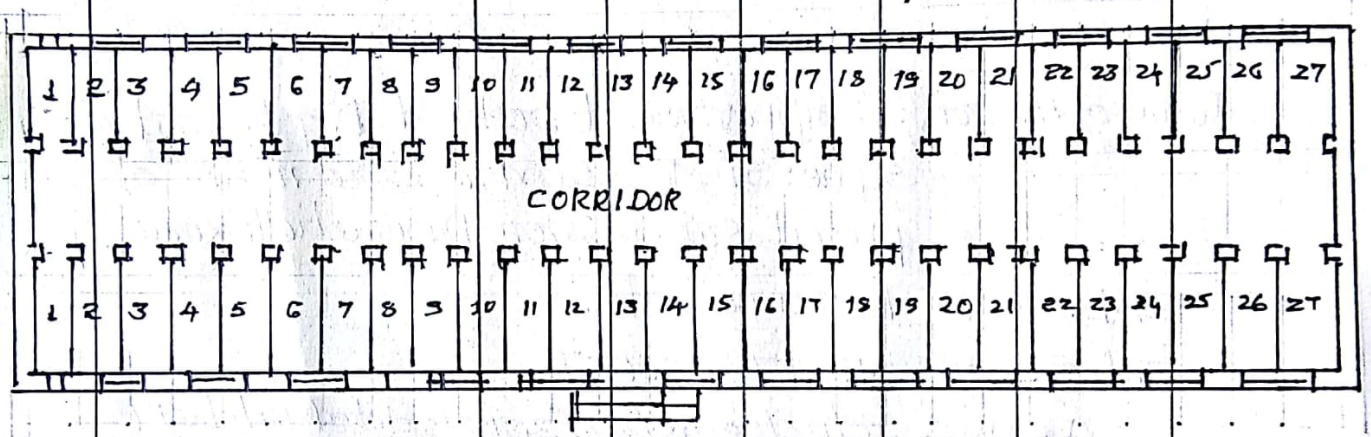

Asst. Executive Engineer
Project Sub Division-II
Dasarahalli Zone,
Bruhat Bengaluru Mahanagara Palike

Scanned by CamScanner

MEASUREMENT BOOK

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
5)	Providing and constructing granite/trap/basalt size stone masonry in foundation with cement mortar 1:6 Stones hammer dressed in courses not less than 20cms high bond stones at 2mts apart in each course including cost of materials etc complete etc complete BF Premeasurement Recorded in this MB Vide page No: 190063 i.e 195.10 M^3 @ Rate . Rs 4521.96 /M^3 Rs 882234=40						
6)	Filling available excavated earth (excluding rock) in sides of foundations up to plinth in layers not exceeding 20cms in depth each deposited layer compacted by ramming after watering etc complete as per specification.						

Asst. Executive Engineer
Project Sub Division-I
Doddaballi Zone.

Scanned by CamScanner

MEASUREMENT BOOK

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
	Scaffolding curing complete as per specification.						
	Main wall	4	30.00	0.23	2.55	70.38	
		4	9.40	0.23	2.58	21.62	
	Side walls	2	6.00	0.23	2.50	6.90	
						98.90	
	a) Deductions						
	D	1.20	1.20	0.23	2.40	1.32	
	D_1	50	0.75	0.23	2.40	20.70	
	W	2	1.75	0.23	1.00	0.81	
	W_1	27	2.00	0.23	0.60	7.45	
		4	0.70	0.23	0.60	0.39	
					(-)	30.67	
	Parapet wall						
	North side	1	7.00	0.23	1.00	1.61	
	South side	1	7.00	0.23	1.00	1.61	
	West side	1	30.00	0.23	1.00	6.90	

EXECUTIVE ENGINEER (Proje
Project Division
Bruhat Bangalore Mahana
Dasarahalli Zone, Bang

Scanned by CamScanner

MEASUREMENT BOOK

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
	out of hot dipped galvanised iron of nominal thickness 0.35 mm etc complete as per specification						
	Partition walls -	27	1.75	—	1.80	85.05	
		27	1.75	—	1.80	85.05	
	Parapet wall East Side -	1	30.00	—	1.00	30.00	
		1	9.40	—	1.00	9.40	
						209.50 M^2	
	@ Rate Rs 1007.64/M^{-2}					Rs	211100=58
							3479 870
					Sub Total Rs		38,13,307=67
					Add KRIDL charges @ 11% Rs		382 785 3,86,463=96
					Grand total Rs		38,99,771=53
							3862656

Asst. Executive Engineer
Project Sub Division-I
Dasarahalli Zone,

Scanned by CamScanner

M.A.R. 57 (Rule 116)

190021

Measurement Book

No. C/09

Serial No.....

Name of work.....From.....To.....

Name of Contractor of nature of Agency.....

Date of commencement of work.....

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
	Certificate 1. Certify that the Contractor completes the work Satisfactorily 2. Certify that the Contractor cleared all debris @ work spot 3/8/18 Asst. Executive Engineer Project Sub Division-I Dasarahalli Zone, Bruhat Bengaluru Mahanagara Palike					3/8/2018	

Scanned by CamScanner
